



October 7, 2013

Thomas Neidecker
Ruscilli Construction Co Inc
2041 Arlingate Lane
Columbus, Ohio 43228

**RE: Storm Water Inspection at Nestle QAC Building Addition/ Franklin County.
Permit #: 4GC04217*AG**

Dear Mr. Neidecker,

This letter is written in follow up to a construction storm water inspection by Jerome Hoke and Elizabeth Pleta, of the Ohio EPA, at Nestle QAC Building Addition located at 6625 Eiterman Road on September 17, 2013. The purpose of the inspection was to evaluate compliance with Ohio EPA's General Storm Water Permit Associated with Construction Activities. During the inspection, we noted the following:

Sediment and Erosion Controls


- As noted in our previous inspection, the sediment pond on site lacks a temporary riser and/or skimmer, despite the commencement of major Earth Moving Activities (See Figure 1). The sediment pond requires a temporary riser and/or skimmer within ten (10) days from receipt of this letter or further compliance efforts may be taken on behalf of the Ohio EPA.
- Silt fence is absent adjacent to the stream in the site's extended flood plain (See Figure 2). We discussed with the superintendent on site that, although silt fence along this area was not included in the original site plans, its installation is required to ensure compliance with the General Permit. We also discussed the need to reinstall silt fence on the northeast side of the site that was removed for construction of a headwall. Installation of silt fence is expected within three (3) days from receipt of this letter.

Thomas Neidecker
Ruscilli Construction Co Inc
Page 2

- Be aware the General Permit states that all barren areas which remain idle in excess of 21 days must be protected from erosion within seven days of the last earth disturbing activities. In addition, erosion protection must be implemented for all areas of final grade within seven (7) days.

If you have any questions regarding this letter or the inspection, please do not hesitate to contact me at our Central District Office at (614) 728-3844. Follow up inspections will be conducted to ensure the conditions of the General Permit are continuing to be met.

Sincerely,



For H.K.

Harry Kallipolitis
Storm Water Coordinator
Division of Surface Water
Central District Office

c: Jeff Bohne, Water Quality Supervisor, DSW/CDO
Tom Neidecker, Ruscilli Project Executive



Figure 1: Sediment basin on site requires a temporary riser and/or skimmer.

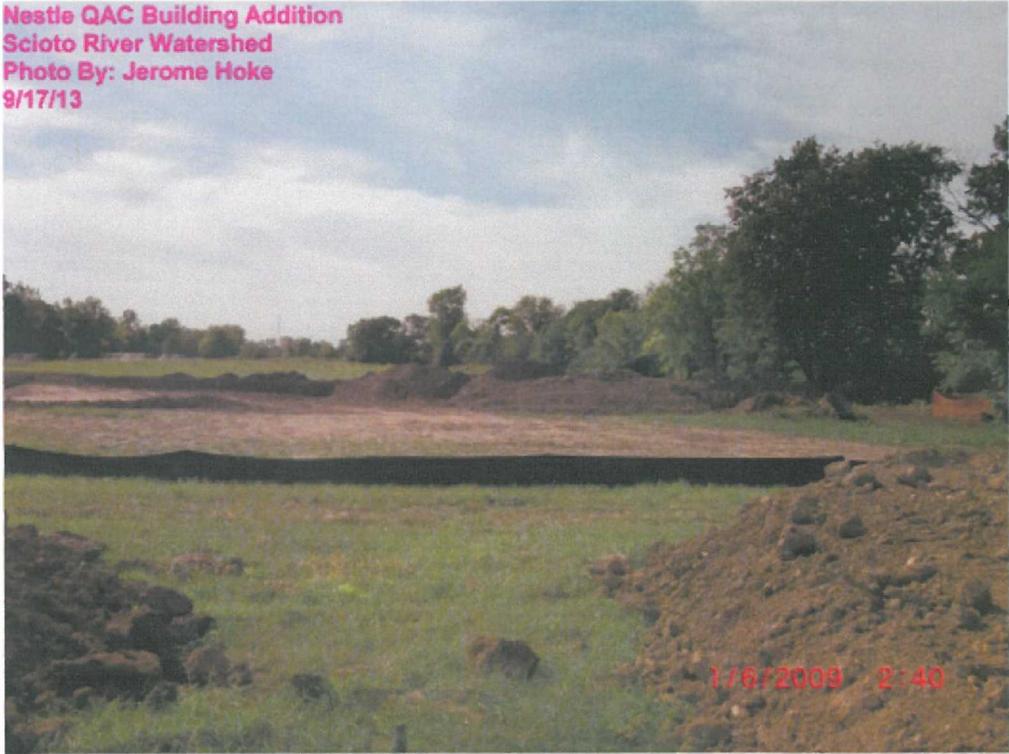


Figure 2: Silt fence is required adjacent to stream by the extended flood plain.
