



Environmental
Protection Agency

John R. Kasich, Governor
Mary Taylor, Lt. Governor
Scott J. Nally, Director

October 11, 2011

Roger Mace
Bloom Carroll Local School District
5240 Plum Road NW
Carroll, OH 43112

Re: Bloom Carroll Middle School / Fairfield County

Dear Mr. Mace:

This letter is written in follow-up to a construction storm water inspection that I conducted at the Bloom Carroll Middle School project located along Beaver Street. The inspection was conducted on September 30, 2011. The reason of the inspection was a follow-up to a previous storm water inspection. During the inspection, the following items were noted:

Sediment and Erosion Controls:

Please install and maintain erosion controls around the construction site. Please see attached pictures.

As stated previously, install a riser on the sediment basin. Sediment impoundments must be utilized for areas of concentrated flow and must be sized with a sediment storage volume of 67 cubic yards per acre of drainage (not disturbance). The sediment *impoundments will require cleaning once they have exceeded 50 percent of their capacity.*

Mud is being tracked on to the road in the front and to the side of the school. Please install erosion controls to prevent mud from being tracked off-site. Please see attached pictures.

If you have any questions regarding this letter or the inspection, please do not hesitate to contact me at our Central District Office at (614) 728-3851.

Sincerely,

Gregory L. Sanders
Environmental Specialist
Division of Surface Water
Central District Office
Enclosure

c: Jeff Bohne, Water Quality Supervisor, DSW/CDO


ec: Gregory L. Sanders, DSW/CDO

GLS/nsm Bloom Carroll MS September 30, 2011


Central District Office
50 West Town Street, Suite 700
P.O. Box 1049
Columbus, OH 43216-1049

614 | 728 3778
614 | 728 3898 (fax)
www.epa.ohio.gov



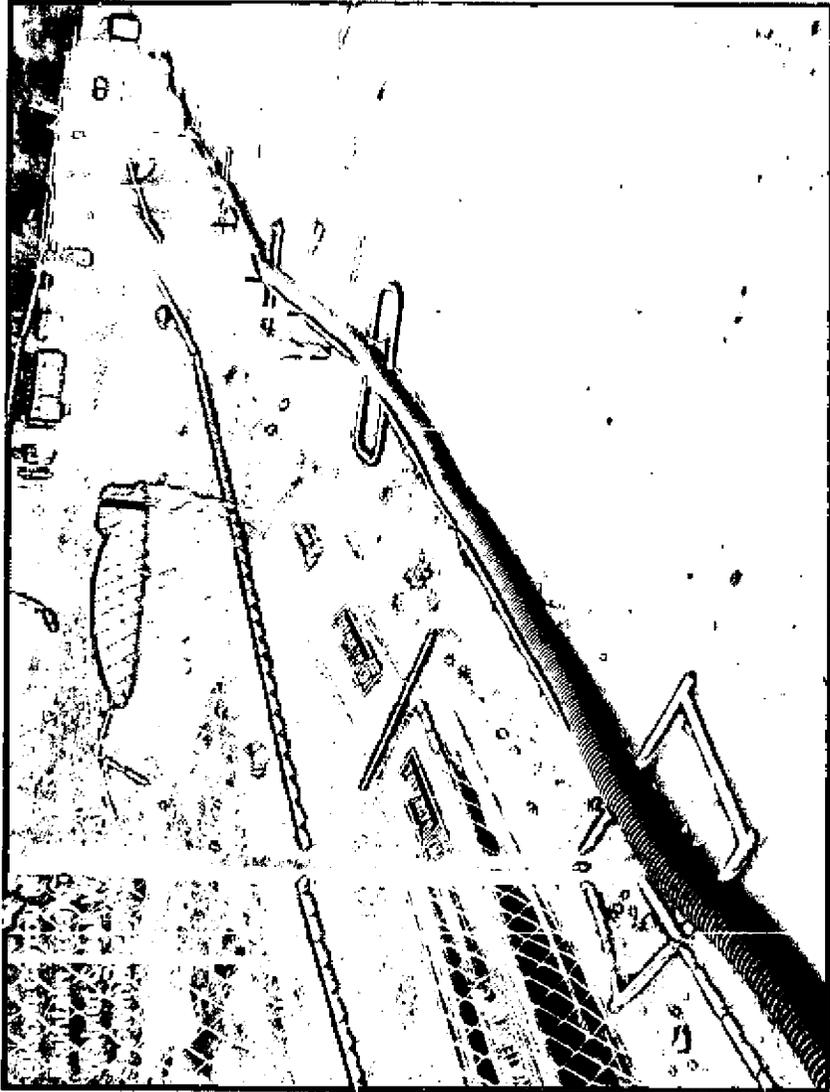



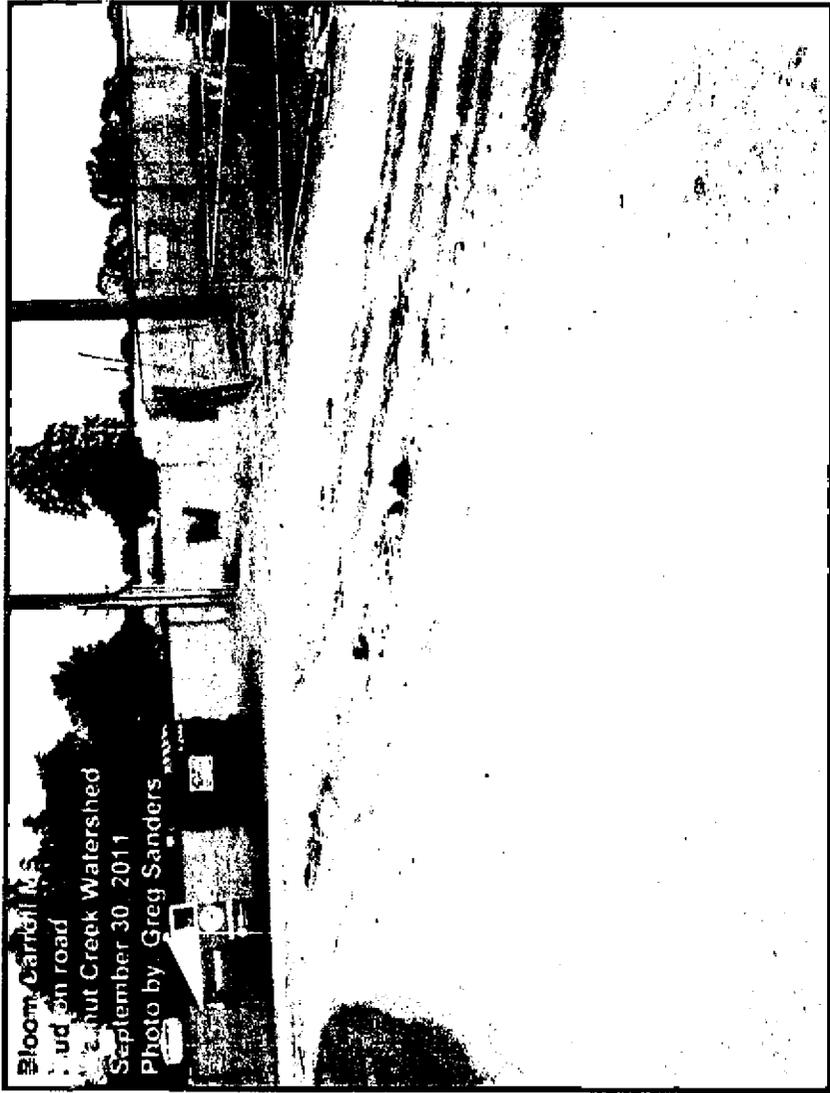

Bloomington, MS
Hudson road
Cahoon Creek Watershed
September 30, 2011
Photo by Greg Sanders

