



State of Ohio Environmental Protection Agency

STREET ADDRESS:

**Central District Office**

MAILING ADDRESS:

W. Lazarus Government Center  
50 W. Town St., Suite 700  
Columbus, Ohio 43215

TELE: (614) 728-3778 FAX: (614) 728-3898  
www.epa.state.oh.us

P.O. Box 1049  
Columbus, OH 43216-1049

July 21, 2010

Lee Bivens  
Ohio Health  
3535 Olentangy River Road  
Columbus, OH 43214

**Re: Construction Storm Water Inspection at Kobacker House / Franklin County  
Permit Number 4GC03284\*AG**

Dear Mr. Bivens:

This letter is written in follow-up to a construction storm water inspection conducted by Elizabeth Schaller and Vinod Tajalpuram of Ohio EPA at the Kobacker House in Columbus, Ohio on July 12, 2010. The purpose of the inspection was to evaluate compliance with the General Storm Water Permit Associated with Construction Activities. The following was noted:

**Sediment and Erosion Control:**

- Perimeter silt fence on northwest side of the hill must be installed and properly maintained to minimize off site sedimentation (see figure 1).
- The currently installed silt fence appears to be functioning as intended. Please be aware the general permit states that all sediment controls will be inspected and maintained every seven days or within 24 hours of a precipitation event equal to or greater than 0.5 inches to ensure continued effectiveness of the sediment basin.
- Inlet protections must be carefully monitored and maintained. This specifically applies to the storm inlets noted adjacent to the entrance (see figure 2).

If you have any questions regarding this letter or my inspection, please do not hesitate to contact me at our Central District Office at 614-728-3844 or email at [harry.kallipolitis@epa.state.oh.us](mailto:harry.kallipolitis@epa.state.oh.us).

Sincerely,

Harry Kallipolitis  
Storm Water Coordinator  
Division of Surface Water  
Central District Office


Enclosure

c: Jeff Bohne, Water Quality Supervisor, DSW/CDO

HK/nsm Kobacker Hours, 7-12-10

Ted Strickland, Governor  
Lee Fisher, Lieutenant Governor  
Chris Korleski, Director





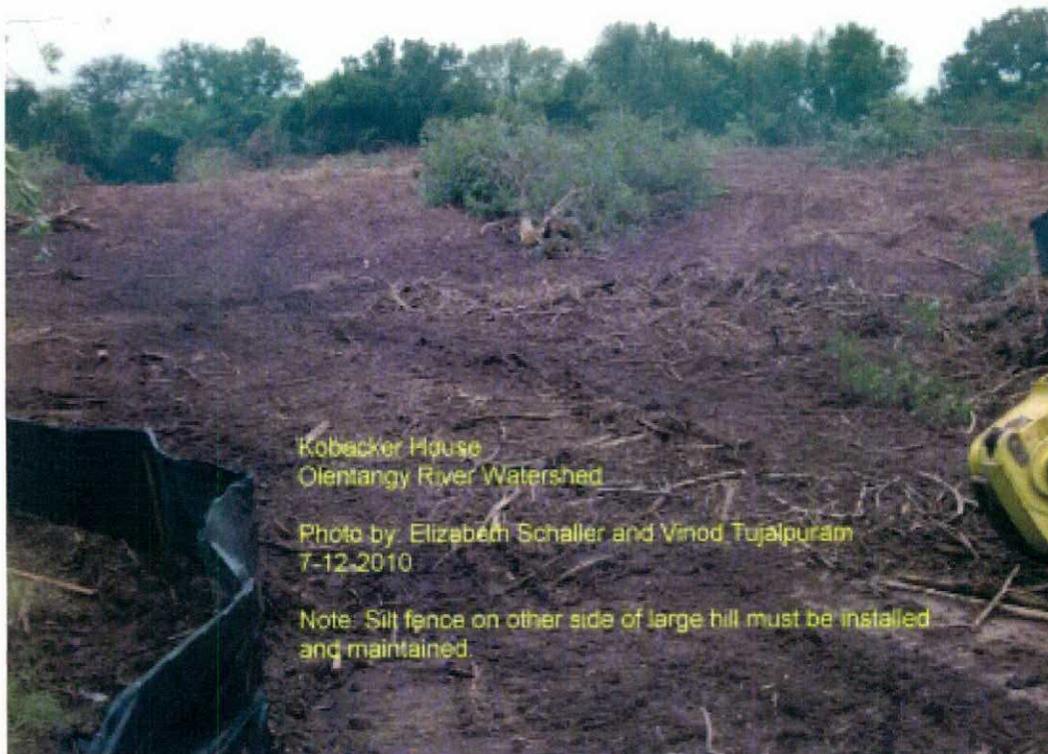


Figure 1: Silt fence must be installed on other side of northwestern hill.



Figure 2: Storm drain covers must be monitored and maintained.



State of Ohio Environmental Protection Agency

STREET ADDRESS:

W. Lazarus Government Center  
50 W. Town St., Suite 700  
Columbus, Ohio 43215

Central District Office

TELE: (614) 728-3778 FAX: (614) 728-3898  
www.epa.state.oh.us

MAILING ADDRESS:

P.O. Box 1049  
Columbus, OH 43216-1049

July 21, 2010

Chuck Evans  
Schottenstein Real Estate Group  
2 Easton Oval #510  
Columbus, OH 43219

Re: **Pre-Construction Storm Water Inspection at Hilliard Grand Apartments /  
Franklin County  
Permit: 4GC03281\*AG**

Dear Mr. Evans:

This letter is written regarding a storm water inspection conducted by Elizabeth Schaller and Abigail Tamkin of Ohio EPA at Hilliard Grand Apartments in Hilliard, Ohio on July 8, 2010. ***It appears construction has not started at this site.*** Ohio EPA has received and approved this site for coverage under the General Storm Water Permit associated with Construction Activities. Ohio EPA's Storm Water Staff will be conducting future storm water inspections to ensure compliance with the General Permit. Please be aware the Agency will be ensuring the following conditions are addressed:

- **Storm Water Pollution Prevention Plan (SWPPP):** A SWPPP must be developed specific for this site. The SWPPP must address the implementation and maintenance of the sediment and erosion controls during all phases of construction. The SWPPP must be updated to reflect the potential dynamics of construction activities. Site maps, depicting drainage patterns and the location of all controls must be inclusive in the SWPPP. The SWPPP must be maintained onsite available for review.
- **Sediment Control Requirements:** The General Permit mandates the installation of appropriate sediment controls as the first step of construction. If the SWPPP depicts the use of a centralized sediment basin for control, the agency will ensure the basin is installed to control all phases of construction. This directly applies to control prior and following the installation of the storm sewer system. Perimeter controls must be installed and maintained.


Ted Strickland, Governor  
Lee Fisher, Lieutenant Governor  
Chris Kortleski, Director



- **Erosion Control Requirements:** Please be aware the General Permit mandates specific permanent and temporary stabilization requirements. All disturbed areas which remain idle in excess of 21 days must be protected from erosion within seven days of the last earth disturbing activities. All areas of final grade must be protected within seven days. All earth disturbing activities should be clearly logged in your inspection reports to ensure the 21 day / seven day requirement is not violated.
- **Maintenance Requirements:** The General Permit requires the permittee to conduct inspections of all sediment and erosion controls every seven days or within 24 hours of a rain event equal to or greater than 0.5 inches. A log of the inspections and resulting corrective actions must be maintained on site available for review. All earth disturbing activities must be clearly documented in your inspection reports to ensure the temporary or permanent stabilization requirements are not violated.
- **Post Construction Requirements:** The General Storm Water Permit requires specific post construction water quality treatment for all sites. Guidance regarding the post construction mandates can be found at: <http://www.epa.state.oh.us/dsw/storm/stormform.aspx>. Please submit to my attention (email preferred at [harry.kallipolitis@epa.state.oh.us](mailto:harry.kallipolitis@epa.state.oh.us)) which practice will be installed at this site to ensure compliance with the General Permit. Please include all design criteria with your submittal.

If you have any questions regarding this letter or the inspection, please do not hesitate to contact me at our Central District Office at (614) 728-3844. Follow-up inspections will be conducted to ensure the conditions of the General Permit are continuing to be met.

Sincerely,



Harry Kallipolitis  
Storm Water Coordinator  
Division of Surface Water  
Central District Office

c: Jeff Bohne, Water Quality Supervisor, DSW/CDO
