



State of Ohio Environmental Protection Agency

**STREET ADDRESS:**

Lazarus Government Center  
50 W. Town St., Suite 700  
Columbus, Ohio 43215

**Central District Office**

TELE: (614) 728-3778 FAX: (614) 728-3898  
www.epa.state.oh.us

**MAILING ADDRESS:**

P.O. Box 1049  
Columbus, OH 43216-1049

July 13, 2010

Paul Ryan  
Columbus Regional Airport Authority  
7161 Second Street  
Columbus, OH 43217

**Re: Construction Storm Water Inspection at Rickenbacker Parkway – Phase 2A / Franklin County  
Permit Number 4GC03205\*AG**

Dear Mr. Ryan:

This letter is written in follow-up to a construction storm water inspection conducted by Stephen Riley and Elizabeth Schaller of Ohio EPA at Rickenbacker Parkway – Phase 2A, "A" Avenue from Lockbourne Eastern Road to Port Road, Columbus, Ohio on July 6, 2010. The purpose of the inspection was to evaluate compliance with the General Storm Water Permit Associated with Construction Activities. During the inspection, our staff noted the following issues associated with construction activities at this site:

**Sediment and Erosion Control:**

- Silt fences on southeast end of the site along Port Road require repair to ensure effective sediment and erosion control. (See figure 1-2)
- Pre-existing storm drains must be adequately protected with silt fences. Sediment laden flows are currently by-passing controls noted in figure 3.
- A by-pass was noted on the outlet structure noted in figure 3. The small orifice at the base of structure must be protected/covered to ensure effective sediment control and eliminate the by-pass.

If you have any questions regarding this letter or my inspection, please do not hesitate to contact me at our Central District Office at 614-728-3844 or email at [harry.kallipolitis@epa.state.oh.us](mailto:harry.kallipolitis@epa.state.oh.us).


Sincerely,

Harry Kallipolitis  
Storm Water Coordinator  
Division of Surface Water  
Central District Office

c: Jeff Bohne, Water Quality Supervisor, DSW/CDO


HK/nsm Rickenbacker Parkway, Phase 2A

Ted Strickland, Governor  
Lee Fisher, Lieutenant Governor  
Chris Korleski, Director






**Figure 1: Poorly trenched silt fence**

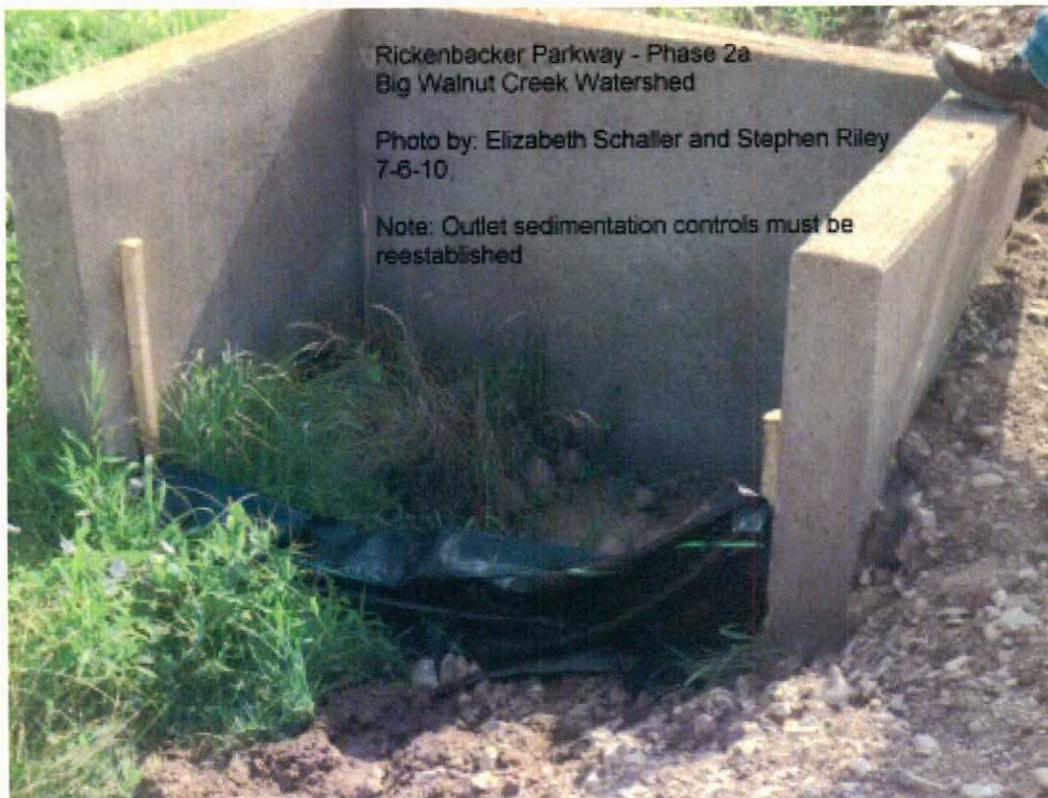

**Figure 2: Insuffienct outlet controls**



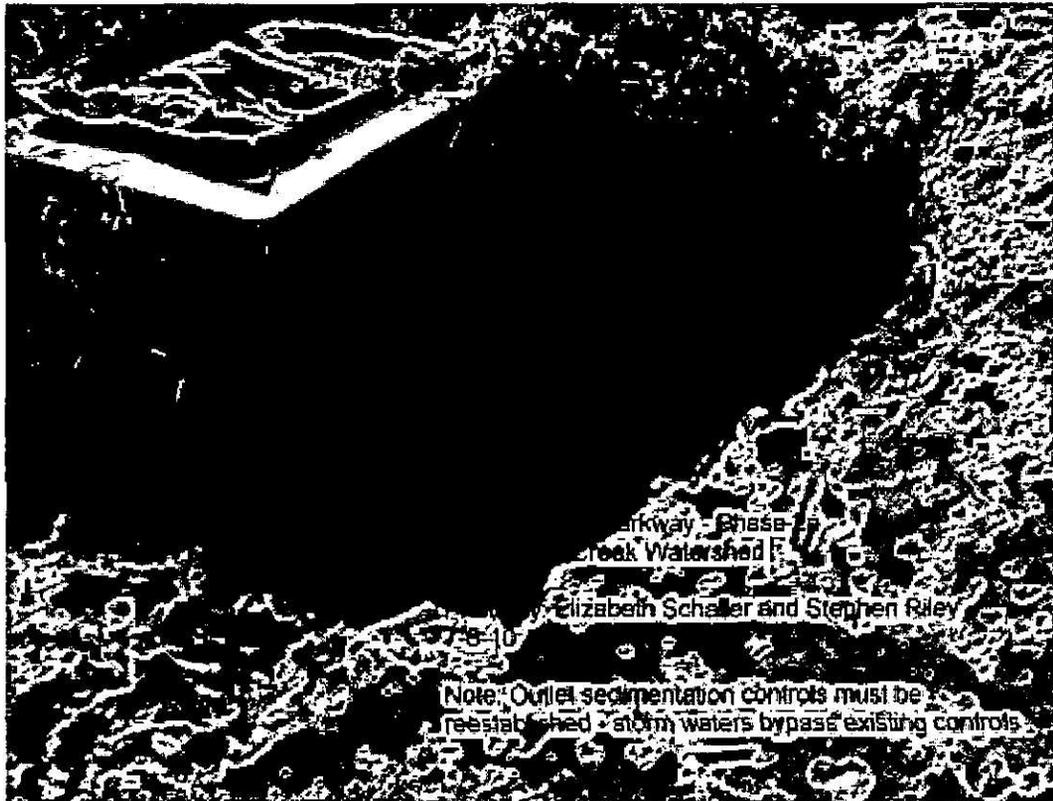


Figure 3: Insufficient outlet controls

