

**Environmental
Protection Agency**

John R. Kasich, Governor
Mary Taylor, Lt. Governor
Scott J. Nally, Director

June 1, 2011


Re: Jackson County
City of Jackson WWTP
0PD00008*ID
Correspondence (PWW)

Mayor and Council
City of Jackson
145 Broadway Street
Jackson, Ohio 45640

Dear Mayor and Council Members:

On May 19, 2011, I conducted a Compliance Evaluation Inspection (CEI) at the City's Wastewater Treatment Plant. Mike Gambino represented the City during the inspection. The purpose of the inspection was to determine the City's compliance with the terms and conditions of its National Pollutant Discharge Elimination System (NPDES) permit.

I reviewed the self-monitoring reports since January 2009. The Total Phosphorous values are shown below.

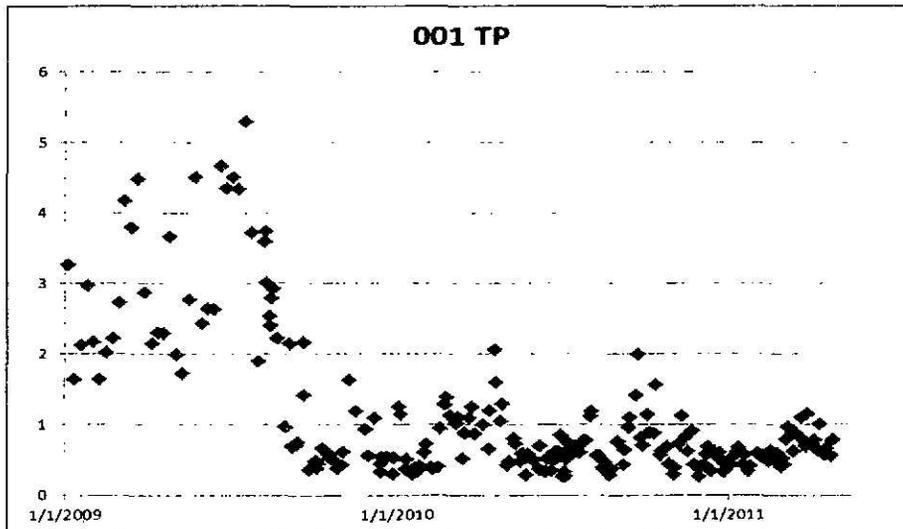

The 7day limit is 1.5mg/L while the monthly limit is 1.0mg/L with limits taking effect August 1, 2009.

The review indicated the following violations of the conditions of your NPDES permit since August 1, 2009.

Station	Reporting Code	Parameter	Limit Type	Limit	Reported Value	Violation Date
001	00665	Phosphorus, Total (P)	30D Conc	1.0	2.78111	8/1/2009
001	00665	Phosphorus, Total (P)	7D Conc	1.5	1.89	8/1/2009
001	00665	Phosphorus, Total (P)	30D Qty	14.3	24.3801	8/1/2009
001	50060	Chlorine, Total Residual	1D Conc	0.02	.06	8/6/2009
001	00665	Phosphorus, Total (P)	7D Conc	1.5	3.43667	8/8/2009
001	00665	Phosphorus, Total (P)	7D Qty	21.5	36.1673	8/8/2009
001	00665	Phosphorus, Total (P)	7D Conc	1.5	2.655	8/15/2009
001	00665	Phosphorus, Total (P)	7D Conc	1.5	2.21	8/22/2009
001	00665	Phosphorus, Total (P)	30D Conc	1.0	1.145	9/1/2009
001	00665	Phosphorus, Total (P)	7D Conc	1.5	1.55	9/1/2009
001	50060	Chlorine, Total Residual	1D Conc	0.02	.13	9/3/2009
001	00665	Phosphorus, Total (P)	7D Conc	1.5	1.62	11/8/2009
001	00665	Phosphorus, Total (P)	30D Conc	1.0	1.25571	4/1/2010
001	00665	Phosphorus, Total (P)	7D Conc	1.5	1.82	4/15/2010
001	31616	Fecal Coliform	7D Conc	2000	9203.27	5/1/2010
001	50060	Chlorine, Total Residual	1D Conc	0.02	.13	7/19/2010
001	00610	Nitrogen, Ammonia (NH3)	30D Conc	1.6	1.94107	9/1/2010
001	00610	Nitrogen, Ammonia (NH3)	7D Conc	2.4	8.13533	9/1/2010
001	00610	Nitrogen, Ammonia (NH3)	7D Qty	34.4	42.2045	9/1/2010
001	50060	Chlorine, Total Residual	1D Conc	0.02	.12	10/18/2010
001	01119	Copper, Total Recoverable	30D Conc	9.4	20.3	1/1/2011
001	01119	Copper, Total Recoverable	30D Qty	0.13	.16704	1/1/2011
001	01119	Copper, Total Recoverable	1D Conc	14	20.3	1/4/2011
001	00530	Total Suspended Solids	7D Qty	215	274.538	3/8/2011
001	00665	Phosphorus, Total (P)	7D Qty	21.5	22.1440	3/8/2011
001	00530	Total Suspended Solids	7D Qty	215	286.473	4/8/2011

The City has provided appropriate non-compliance notifications for the above violations and addressed non-compliance with fine tuning plant operations. Additionally, a wet spring in 2011 has led to sustained elevated flows.

The plant has a list of maintenance activities they are working on including #3 sewage pump, (2 permeate pumps, 2 RAS pumps, and some valve replacements on the new MBR plant). The new fine screens appear to have some corrosion along with valving issues that are also being looked into.

The City reports Sanitary Sewer Overflows for blockages, etc. in accordance with the NPDES permit. For calendar year 2010 there were twenty-three reported SSOs. For 2011, twenty incidents have occurred as of end of April.

The facility appeared to be operating in compliance. As a courtesy reminder, the NPDES renewal OPD00008*JD becomes effective June 1, 2011.

You may call me at (740) 380-5272 if you have any questions regarding this letter or any other concerns with Ohio EPA regulations.

Sincerely,



Aaron Pennington
District Representative
Division of Surface Water

AP/dh

Enclosure

c: Mike Gambino, Superintendent, City of Jackson WWTP

NPDES
Compliance Inspection Report

A. NATIONAL DATA SYSTEM CODING

Permit No.	NPDES No.	Date	Inspection Type	Inspector	Facility Type
OH0020834	OPD00008*JD	May 19, 2011	CEI	S	I

B. FACILITY DATA

Name & Location of Facility Inspected	Entry Time	Permit Effective Date
City of Jackson WWTP 225 Wood Avenue Jackson, OH 45640	~9:00 A.M.	August 1, 2010
	Exit Time	Permit Expiration Date
	~1:45 P.M.	January 31, 2011

Name(s) & Title(s) of On-Site Representative(s)	Phone Number(s)
Mike Gambino, WWTP Supintendant	(740)-286-1137
Name, Address, & Title of Responsible Official	Phone Number
Mayor and Council	


C. AREAS EVALUATED DURING INSPECTION

<u> S </u> Permit	<u> S </u> Flow Measurement	<u> N </u> Pretreatment
<u> S </u> Records/Reports	<u> S </u> Laboratory	<u> S </u> Compliance Schedules
<u> S </u> Operations & Maintenance	<u> S </u> Effluent/Receiving Waters	<u> S </u> Self-Monitoring Program
<u> S </u> Facility Site Review	<u> S </u> Sludge Storage/Disposal	<u> </u> Other
<u> M </u> Collection System		

(S = Satisfactory; M = Marginal; U = Unsatisfactory; N = Not Evaluated; N/A = Not Applicable)

D. SUMMARY OF FINDINGS/COMMENTS (attach additional sheets if necessary)

See Cover Letter



Aaron M. Pennington, Inspector, Ohio EPA, Southeast District Office

5-25-11
Date



Timothy M. Campbell, Reviewer, Ohio EPA, Southeast District Office

5/31/11
Date

E. PERMIT VERIFICATION

Inspection Observations Verify the Permit	YES	NO	N/A	N/E
a. Correct name & mailing address of permittee	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
b. Correct name & location of receiving waters	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
c. Product(s) & production rates conform with permit application (industries)	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
d. Flows & loadings conform with NPDES permit	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
e. Treatment processes are as described in permit application/briefing memo	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
f. New treatment process(es) added since last inspection	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
g. Notification given to state of new, different, or increased discharges	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
h. All discharges are permitted	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
i. Number & location of discharge points are as described in permit	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Comments:

Daily flows have been elevated through the wet spring.

COMPLIANCE SCHEDULES/VIOLATIONS

	YES	NO	N/A	N/E
a. Any significant violations since the last inspection	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
b. Permittee is taking actions to resolve violations	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
c. Permittee has compliance schedule	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
d. Compliance schedule contained in: <u>Permit</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
e. Permittee is meeting compliance schedule	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Comments:

G. OPERATION AND MAINTENANCE

Treatment Facility Properly Operated & Maintained	YES	NO	N/A	N/E
a. Standby power available: Generator: <input checked="" type="checkbox"/> Dual Feed: <input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
b. Adequate alarm system available for power or equipment failures	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
c. All treatment units in service other than backup units	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
d. Sufficient operating staff provided: # of shifts: <u>1</u> Days/Week: <u>7</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
e. Operator holds unexpired license of class required by permit. Class: <u>III</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
f. Copy of certificate of Operator of Record displayed on-site	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
g. Minimum operator staffing requirements fulfilled (OAC 3745-7)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
h. Routine & preventive maintenance schedule/performed on time	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
i. Any major equipment breakdown since last inspection	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
j. Operation & maintenance manual provided & maintained	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
k. Any plant bypasses since last inspection	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
l. Regulatory agency notified of bypasses: On MORS: <input type="checkbox"/> 800 No.: <input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
m. Any hydraulic and/or organic overloads experienced since last inspection	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Comments:

Wet weather has led to some extended hydraulic overload.
#3 Main sewage pump went down, along with 2 permeate and RAS pumps on the MBR plant.

Record Keeping	YES	NO	N/A	N/E
a. Log book provided	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
b. Log book kept on-site	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
c. Log book contains the following:	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
1. Identification of treatment works	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
2. Date/Time of arrival/departure of ORC	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
3. Daily record of operation and maintenance activities	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
4. Laboratory results (unless documented on bench sheets)	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
5. Identification of person making log entries	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
d. Is the ORC submitting written notification to Ohio EPA and permittee when a collection system overflow, treatment plant bypass or effluent limit violation has occurred.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Comments:

Collection System	YES	NO	N/A	N/E
a. Percent combined system. Percent: _____	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
b. Any collection system overflows since last inspection: CSO: <input type="checkbox"/> SSO: <input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
c. Regulatory agency notified of overflow (SSOs)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
d. CSO O&M plan provided and implemented	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
e. CSOs monitored and reported in accordance with permit	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
f. Portable pumps used to relieve system	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
g. Lift station alarm systems provided and maintained	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
h. Are lift stations equipped with permanent standby power or equivalent	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
i. Is there an inflow/infiltration problem (separate sewer system), or were there any major repairs to collection system since last inspection	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
j. Any complaints received since last inspection of basement flooding	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
k. Are any portions of the sewer system at or near capacity	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Comments:

Looking to install a force main extension where Holly Green and McCarty Lane Lift Stations combine

H. SLUDGE MANAGEMENT

	YES	NO	N/A	N/E
a. Sludge adequately disposed. Method: <u>Land Application</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
b. If sludge is incinerated, where is ash disposed of? _____	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
c. Is sludge disposal contracted? Name: _____	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
d. Has amount of sludge generated changed significantly since last inspection	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
e. Adequate sludge storage provided at facility	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
f. Land application sites monitored and inspected per state rules	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
g. Records kept in accordance with state rules	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
h. Any complaints received in last year regarding sludge	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
i. Is sludge adequately processed (digestion, dewatering, pathogen control) in accordance with Ohio EPA rules	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Comments:

Looking to install drying beds to provide storage for extended cold/wet periods

I. SELF-MONITORING PROGRAM

Part 1 – Flow Measurement	YES	NO	N/A	N/E
a. Primary flow measuring device properly operated & maintained. Type of device: <input type="checkbox"/> Ultrasonic & parshall flume <input type="checkbox"/> Calculated from influent <input type="checkbox"/> Weir <input checked="" type="checkbox"/> Other <input checked="" type="checkbox"/> Ultrasonic & weir specify: <u>Magmeter</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
b. Calibration frequency adequate. Date of last calibration: <u>12-3-10</u>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
c. Secondary instruments (totalizers, recorders, etc.) properly operated and maintained	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
d. Flow measurement equipment adequate to handle expected ranges of flows	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
e. Actual flow discharged is measured	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
f. Flow measuring equipment inspection frequency: <input checked="" type="checkbox"/> Daily <input type="checkbox"/> Monthly <input type="checkbox"/> Weekly <input type="checkbox"/> Other				

Comments:

2 separate effluent meters from the 2 plants (MBR and Oxidation Ditch)

Part 2 - Sampling	YES	NO	N/A	N/E
a. Sampling location(s) are as specified by permit	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
b. Parameters and sampling frequency agree with permit	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
c. Permittee uses required sampling method	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
d. Sample collection procedures are adequate	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
i. Samples refrigerated during compositing	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
ii. Proper preservation techniques used	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
Conform with 40 CFR 136.3	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
e. Monitoring records (e.g., flow, pH, D.O., etc.) maintained for a minimum of three years including all original strip chart recordings (e.g., continuous monitoring instrumentation, calibration, & maintenance records)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
f. Adequate records maintained of sampling date, time, exact location, etc.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

Comments:

Part 3 – Laboratory, General	YES	NO	N/A	N/E
a. Written Standard Operating Procedures (SOPs) for all analysis performed on-site	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
b. EPA approved analytical testing procedures used (40 CFR 136.3)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
c. If alternate analytical procedures are used, proper approval has been obtained	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
d. Analysis being performed more frequently than required by permit	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
e. If (c) is yes, are results reported in permittee's self-monitoring report	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
f. Commercial laboratory used: 1. Parameters analyzed by commercial lab: <u>Metals, Bioassay</u> 2. Lab name: <u>Belmont labs, Ginosko Laboratory, Enviroscience</u>				

Comments:

General Lab Criteria

Facility: City of Jackson WWTP

Criteria	Standard Methods Requirement	Acceptable?	Rating
Balance		<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
• Standard Weights	• Either NIST Class s or ASTM/ANSI Class 1 weights ^{1,2}	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Calibration Frequency/ Documentation	• Calibration verification required at least once each day the balance is used ³	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Cleanliness, air movement, vibration	• Cleanliness of balance is a must and air movement and vibration needs to be kept to a minimum ¹	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Other	• Service and recalibrate annually (manufacturer representative or comparable) ¹	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Must be able to measure to 0.1 grams ⁴	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Instrument manual available	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Log book maintained ⁶	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

Criteria	Standard Methods Requirement	Acceptable?	Rating
Drying Oven (Suspended Solids)		<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
• Temperature Recordkeeping	• Temperature recorded with each use ⁴	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Log book maintained ⁶	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Calibration Frequency/ Documentation	• Thermometer calibrated annually with NIST traceable thermometer ^{1,2} . Correction factor posted on thermometer/equipment ¹	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Other	• Thermometer temperature in 0.1°C increments ⁵	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Acceptable temperature range is 103° – 105°F ⁴	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Instrument manual available	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

Criteria	Standard Methods Requirement	Acceptable?	Rating
pH Meter		<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
• Calibration Frequency/ Documentation	• Calibration verification required for testing over long period of time (e.g. 12 hrs.), or after a large number of samples (every 10 samples) ³	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Log book maintained ⁹	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Minimum of 2 point calibration	• Calibration per manufacturer specification and calibration buffers must bracket anticipated result ⁷	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Slope Documentation/ Acceptability	• Slope acceptable range indicated on benchsheet ²	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Buffer Expiration Date	• Buffers must not be expired	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
• Other	• Instrument manual available	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Teflon covered magnetic stirrer or equivalent for mixing ⁸	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

General Lab Criteria

Criteria	Standard Methods Requirement	Acceptable?		Rating
Dissolved Oxygen Meter		Acceptable?		A
• Calibration Method	• Air or known DO calibration method ¹⁰	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Calibration per manufacturer specification ¹⁰	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
• Calibration Frequency/ Documentation	• Logbook maintained ⁹	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Calibration verification required at least once each day the meter is used. ³	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
• Other	• Small to no bubble present under membrane (must be smaller than the lead in number 2 pencil) ¹¹	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Instrument manual available	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
Comments:				

Criteria	Standard Methods Requirement	Acceptable?		Rating
Incubator (CBOD/E-Coli)		Acceptable?		A
• Temperature Recordkeeping	• Temperature checked/recorded twice daily for each shelf in use ¹	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Temperature checked/recorded daily ² (CBOD)	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Acceptable temperature range (CBOD) is 20°C ±1.0° ¹²	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Acceptable temperature range (E-Coli) is 35°C ±0.5° ²²	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Logbook maintained ⁹	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
• Temperature Calibration/ Documentation	• Thermometer calibrated annually with NIST traceable thermometer ^{1,2}	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Temperature correction information posted on incubator ¹	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
• E-Coli can use multiple tubes (five 20 ml or ten 10 mg), or mfg's multi-well tray	• E-coli Ultraviolet lamp (365 nm wave length, 6 W bulb) ²³	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
• Other	• Instrument manual available	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Temperature Log (thermometer reads to 0.1 Celsius) ⁵	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
Comments:				

Criteria	Standard Methods Requirement	Acceptable?		Rating
Refrigerator		Acceptable?		A
• Temperature Recordkeeping	• Temperature Log (thermometer reads to 0.1 Celsius) ⁵	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
• Temperature Calibration/ Documentation	• Thermometer calibrated annually with NIST traceable thermometer ^{1,2}	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
• Other	• Thermometer held in water bath ¹	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Refrigerator temperature ±0.6° Celsius ¹³	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
	• Do not store volatile solvents, food, or beverages ¹⁴	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
Comments:				

Criteria	Standard Methods Requirement	Acceptable?		Rating
Chlorine Meter		Acceptable?		A
• Calibration Frequency/ Documentation	• pH/millivolt meter read to 0.1 mV ¹⁵	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No	
		• Calibration verification required for testing over long period of time (e.g. 12 hrs.), or after a large number of samples (every 10 samples) ³	<input checked="" type="checkbox"/> Yes	<input type="checkbox"/> No

General Lab Criteria

<ul style="list-style-type: none"> • Calibration Method 	<ul style="list-style-type: none"> • Calibration using three iodate solutions 0.2, 1.0, 5.0 milliliters or calibration per manufacturer specification¹⁶ • Standards used for calibration not expired 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
<ul style="list-style-type: none"> • Slope Documentation/ Acceptability 	<ul style="list-style-type: none"> • Calibration curve (acceptable slope) 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
<ul style="list-style-type: none"> • Other 	<ul style="list-style-type: none"> • Electrode free of deposits and foreign material • Log book being maintained⁹ • Instrument manual available 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

Criteria	Standard Methods Requirement	Acceptable?	Rating
Ammonia Meter			
<ul style="list-style-type: none"> • Calibration Frequency/ Documentation 	<ul style="list-style-type: none"> • Calibration verification required for testing over long period of time (e.g. 12 hrs.), or after a large number of samples (every 10 samples)³ • Log book being maintained⁹ 	<input type="checkbox"/> Yes <input type="checkbox"/> No	NR
<ul style="list-style-type: none"> • Slope Acceptability 	<ul style="list-style-type: none"> • Verify calibration slope is acceptable (per mfg. spec.) 	<input type="checkbox"/> Yes <input type="checkbox"/> No	
<ul style="list-style-type: none"> • Calibration Method 	<ul style="list-style-type: none"> • Standards used for calibration (3 ammonia solutions of 10 mg/l, 1 mg/l, and 0.1 mg/l) or per mfg. spec.¹⁷ • Standards used for calibration not expired 	<input type="checkbox"/> Yes <input type="checkbox"/> No	
<ul style="list-style-type: none"> • Other 	<ul style="list-style-type: none"> • Electrode free of deposits and foreign material • Teflon covered magnetic stirrer or equivalent for mixing¹⁸ • Instrument manual available 	<input type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

Criteria	Standard Methods Requirement	Acceptable?	Rating
Sample Collection/Handling			
<ul style="list-style-type: none"> • Sample Labeling 	<ul style="list-style-type: none"> • Samples container labeled (description, date, time, preservative added, initialed)¹⁹ 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
<ul style="list-style-type: none"> • Chain of Custody 	<ul style="list-style-type: none"> • Chain of custody (description, date, time, signature)¹⁹ 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
<ul style="list-style-type: none"> • Other 	<ul style="list-style-type: none"> • Composite samples refrigerated during sample collection¹⁴ • Equipment blanks utilized¹⁴ • SOP for cleaning of sampling equipment • Log book being maintained⁹ 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

Criteria	Standard Methods Requirement	Acceptable?	Rating
Desiccator			
<ul style="list-style-type: none"> • General Criteria 	<ul style="list-style-type: none"> • Properly working seals • Desiccant fresh (blue color) 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
<ul style="list-style-type: none"> • Documentation 	<ul style="list-style-type: none"> • Log book being maintained⁹ 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

General Lab Criteria

Criteria	Standard Methods Requirement	Acceptable?	Rating
Bench Sheets			
<ul style="list-style-type: none"> • General Criteria 	• Date(s) ²	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
	• Analyst initials ²	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Blue or black ink pen ²	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Calibration information ²	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Equations, calculations, units for all measurements, notations, and results present ²	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	• Corrections, single line through, initialed and dated ²	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

Criteria	Standard Methods Requirement	Acceptable?	Rating
Hot Water Bath (Fecal Coliform/E. Coli)			
<ul style="list-style-type: none"> • Temperature Recordkeeping 	• Temperature Log (thermometer reads 0.2° C) ²¹	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
		• Incubator temperature 44.5° C ±0.2° ^{21/24}	
<ul style="list-style-type: none"> • Temperature Calibration/ Documentation 	• Thermometer calibrated annually with NIST traceable thermometer ^{1,2}	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
		• Log book being maintained ⁹	
<ul style="list-style-type: none"> • Water Level 	• Thermometer total immersion or partial (line on thermometer to ID immersion depth) ^{1,5}	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

Criteria	Standard Methods Requirement	Acceptable?	Rating
Autoclaves/Steam Sterilizers			
<ul style="list-style-type: none"> • All apparatus utilized is adequately sterilized before use 	• Sterilizing temperature 121° C ²⁵	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
		• 10 to 30 minutes time based on material being sterilized ²⁶	
<ul style="list-style-type: none"> • Documentation 	• Verify the autoclave temperature weekly by using a maximum registering thermometer (MRT) to confirm that 121°C has been reached as measured in the exhaust ¹	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
		• Date, contents, sterilization time and temperature, total time in autoclave, and analyst's initials should be recorded each time the autoclave is used ¹	
<ul style="list-style-type: none"> • Temperature Calibration/ Documentation 	• Thermometer calibrated annually with NIST traceable thermometer ^{1,2}	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
		• Log book being maintained ⁹	
<ul style="list-style-type: none"> • Performance Checks 	• Test monthly for efficacy using a biological such as commercially available <i>Geobacillus stearothermophilus</i> in spore strips, suspensions, or capsules ¹	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

General Lab Criteria

Criteria	Standard Methods Requirement	Acceptable?	Rating
Final Effluent Temperature Monitoring			
<ul style="list-style-type: none"> • General Criteria 	<ul style="list-style-type: none"> • Thermometer calibrated annually with NIST traceable thermometer^{1,2} 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	A
	<ul style="list-style-type: none"> • Thermometer reads in increments of at least 0.1°C⁵ 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
	<ul style="list-style-type: none"> • Log book being maintained² 	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	
Comments:			

Number of Criteria Rated:	Acceptable	13
	Marginal	
	Unacceptable	
	Total Number of Areas Rated	13

Acceptable Ratings – No action required (recommend SOP's written or updated, perform DMRQA's for all onsite analysis, recommend voluntary lab analyst certification, written response not required).

Marginal Ratings – Improvements required, written response required (recommend SOP's be written or updated, recommend perform DMRQA's for all onsite analysis, recommend voluntary lab analyst certification, require deficiencies to be addressed in written response).

Unsatisfactory Rating – Improvements required, written response required, NOV issued (recommend SOP's be written or updated, recommend they perform DMRQA's for all onsite analysis, recommend voluntary lab analyst certification, require deficiencies to be addressed in written response to NOV).

Consider recommending PAI Audit from DES when:

- >60% of ratings are Marginal
- >45% of ratings are a combination of Marginal or Unacceptable
- >30% of ratings are Unacceptable

General Lab Criteria

Notation of Referenced Method

1 Method 9020-B, Item 4	14 Method 1060A, Item 1
2 Method 1020-A, Item 1	15 Method 4500-CI I, Item 2
3 Method 1020-B, Item 10	16 Method 4500-CI I, Item 4
4 Method 2540-B, Item 2	17 Method 4500-NH3 D, Item 4
5 Method 2550-B, Item 1	18 Method 4500-NH3 D, Item 2
6 Method 1020-B, Item 1	19 Method 1060-B, Item 2
7 Method 4500-H B, Item 4	20 Method 1060-B, Item 1
8 Method 4500-H B, Item 2	21 Method 9222D, Item 1
9 Method 1020-B, Item 2	22 Method 9223 B, Item 2
10 Method 4500-O B, Item 3	23 Method 9223 B, Item 3
11 Method 4500-O G, Item 3	24 Method 1603, Item 2
12 Method 5210-B, Item 5	25 Method 9030-B, Item 3
13 CFR 136.3, Table II	26 Method 9020 B, Table IV

Equipment Logbook Content – All maintenance performed on a piece of equipment should be documented in the logbook. This should include parts replacement and routine maintenance activities. Entries should include date, maintenance performed and initials of person making entry.

Preservation and Holding Times						
Parameter	Container	Min. Sample Size (mL)	Sample Type	Preservation	Maximum Storage Time	
					Recommended	Regulatory
BOD / CBOD	P, G	1000	G, C	Refrigerate ≤6°C	6h	48h
TSS	P, G	200	G, C	Refrigerate ≤6°C	7 d	7 d
pH	P, G	50	G	Analyze immediately	0.25h	0.25 h
NH3-N	P, G	500	G, C	Analyze as soon as possible or add H ₂ SO ₄ to pH <2, Refrigerate ≤6°C	7 d	28 d
TRC	P, G	500	G	Analyze immediately	0.25h	0.25 h
DO (electrode)	G, BOD Bottle	300	G	Analyze immediately	0.25h	0.25 h
Temperature	P, G	--	G	Analyze immediately	0.25h	0.25 h
Metals, general	P, G	1000	G, C	For dissolved filter immediately and add HNO ₃ to pH <2	6 months	6 months
Purgeables by purge and trap	G (PTFE lined lid)	40 (X2)	G	HCl to pH <2, Refrigerate ≤6°C	7 d	14 d
Base/Neutrals and acids	G (solvent rinsed or baked)	1000	G, C	Refrigerate ≤6°C	7 d	7 days until extraction 40 days after extraction
Pesticides	G (PTFE lined lid)	1000	C	Refrigerate ≤6°C	7 d	7 days until extraction 40 days after extraction
Fecal Coliform / E-Coli	G, P (Sterilized)	100	G	Refrigerate ≤10°C If chlorine present, add sodium thiosulfate tablet	6 hrs transport. Start analysis within 2 hrs of receipt in lab.	
Oil and Grease	G	1000	G	HCl or H ₂ SO ₄ to pH <2, Refrigerate ≤6°C	28 d	28 d

General Lab Criteria

Approved Standard Methods	
CBOD / BOD 5 Day	Std Methods 5210-B
Ammonia, Selective Electrode Method	Std Methods 4500-NH3 D
Total Residual Chlorine, DPD Colorimetric Method	Std Methods 4500-Cl G
Total Suspended Solids, Dried at 103-105°C	Std Methods 2540-D
Dissolved Oxygen, Membrane Electrode Method	Std Methods 4500-O G
pH, Electrometric Method	Std Methods 4500-H+ B
Fecal Coliform, Membrane Filter Procedure	Std Methods 9222D
Escherichia Coli, Enzyme Substrate Test	Std Method 9223B
Escherichia Coli Membrane Filtration Procedure	EPA Method 1603
Oil and Grease	USEPA 1664A or Std Methods 5520B
Metals, general	USEPA 200, Std Methods 3111B or C, or 3120B
Volatiles (Purgeables by purge and trap)	USEPA 6210, Std Methods 624
Semi-Volatiles (Base/Neutrals and acids)	USEPA 6410, Std Methods 625
Pesticides	USEPA 6410 and 6630, Std Methods 608
