



**Environmental  
Protection Agency**

John R. Kasich, Governor  
Mary Taylor, Lt. Governor  
Scott J. Nally, Director

July 12, 2012

David Feusner  
Wendy's Company  
One Dave Thomas Boulevard  
Dublin, Ohio 43017

**Re: Storm Water Inspection at Wendy's Company Office Building & Conference  
Center- Franklin County  
Permit # 4GC03807\*AG**

Dear Mr. Feusner:

This letter is written in follow-up to a construction storm water inspection by Brittany Turner, and Alicia Rector of the Ohio EPA, at Wendy's Company Office Building & Conference Center located at One Dave Thomas Boulevard, Dublin, Ohio on July 2, 2012. The purpose of the inspection was to evaluate compliance with Ohio EPA's General Storm Water Permit Associated with Construction Activities. During the inspection, we noted the following:

**Sediment and Erosion Controls:**

- The sediment controls implemented on west side of this site will require maintenance or reinstallation to ensure a proper functioning condition (See Figure 1).
- Our staff observed an area of concrete disposal that lacked proper containment. If future onsite disposal is required, containment measures such as a pit impoundment is expected (See Figure 2).
- Be aware the General Permit states that all barren areas which remain idle in excess of 21 days must be protected from erosion within seven days of the last earth disturbing activities. In addition, erosion protection must be implemented for all areas of final grade within seven (7) days (See Figure 3).

David Feusner  
Wendy's Company  
Page -2-

If you have any questions regarding this letter or the inspection, please do not hesitate to contact me at our Central District Office at (614) 728-3844. Follow-up inspections will be conducted to ensure the conditions of the General Permit are continuing to be met.

Sincerely,



Harry Kallipolitis  
Storm Water Coordinator  
Division of Surface Water  
Central District Office

c: Eric Williamson, Turner Construction Company

HK/nsm Wendys Co. Office Bldg conference Ctr. Franklin County 7-5-12



**Figure 1 Sediment Controls need Maintained**



**Figure 2 Concrete Washout**

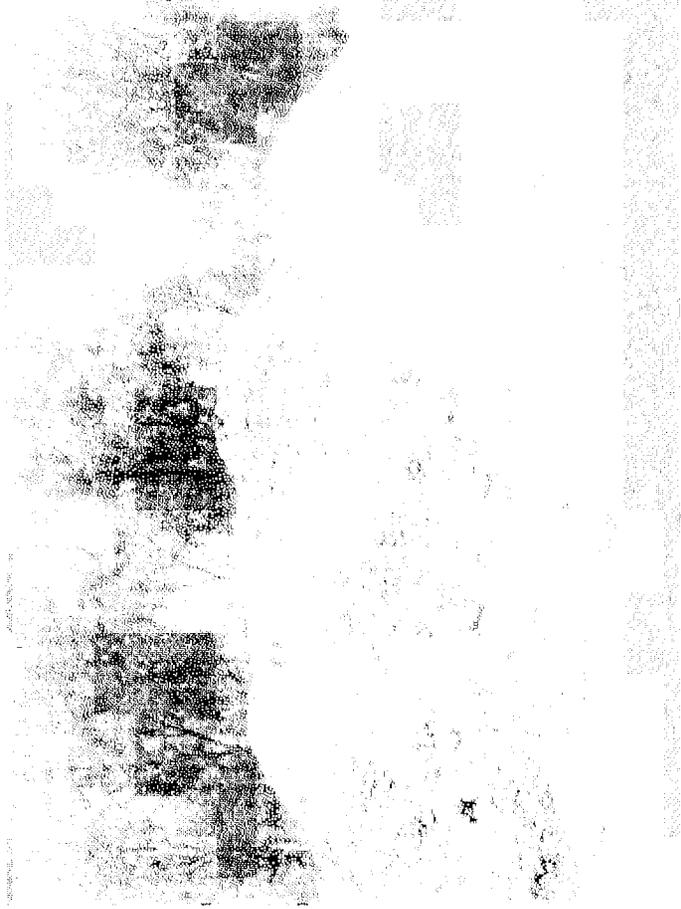


Figure 3 Barren Areas
