



**Environmental
Protection Agency**

John R. Kasich, Governor
Mary Taylor, Lt. Governor
Scott J. Nally, Director

July 18, 2012

Douglas Scholl, AIP
Ohio Health-Riverside Methodist Hospital
550 Metro Place, Suite 600
Dublin, Ohio 43017

**Re: Storm Water Inspection at Riverside Methodist Hospital – Franklin County
Permit # 4GC03863*AG**

Dear Mr. Scholl:

This letter is written in follow-up to a construction storm water inspection by Brittany Turner, Abigail Tamkin of the Ohio EPA, accompanied by Ronald E. Knight Jr. at Riverside Methodist Hospital located at 3535 Olentangy River Road, Columbus, Ohio on July 10, 2012. The purpose of the inspection was to evaluate compliance with Ohio EPA General Storm Water Permit Associated with Construction Activities. During the inspection, we noted the following:

Sediment and Erosion Controls:

- The dandy bag on the Northwest corner of a site located next to the garage requires maintenance at this time to ensure proper functioning condition (See Figure 1).
- The inlet protections at the entrance to the south site must be properly maintained (See Figure 2 & 3).
- The dandy bag near the construction site located next to the garage requires maintenance at this time (See Figure 4).
- The silt fence that runs along West North Broadway must be maintained at this time (See Figure 5).
- The silt fence along West North Broadway must be extended on each side of the stairs in order to ensure compliance with Ohio EPA General Storm Water Permit. (See Figure 6)

- The straw wattles on the northeast side of the south site must be properly reinstalled (See Figure 7).
- Sediment and erosion controls must be maintained in order to ensure proper functioning condition and compliance with Ohio EPA General Storm Water Permit.
- Be aware the General Permit states that all barren areas which remain idle in excess of 21 days must be protected from erosion within seven days of the last earth disturbing activities. In addition, erosion protection must be implemented for all areas of final grade within seven (7) days (See Figure 8)

If you have any questions regarding this letter or the inspection, please do not hesitate to contact me at our Central District Office at (614) 728-3844. Follow-up inspections will be conducted to ensure the conditions of the General Permit are continuing to be met.

Sincerely,



FOR
Harry Kallipolitis
Storm Water Coordinator
Division of Surface Water
Central District Office

cc: ron.knight@whiting-turner.com



Figure 1 Northwest corner dandy bag

Figure 2 Inlet protection required




Figure 3 Inlet protection required
City of Chicago, Department of Public Works
Chicago, Illinois

Figure 3 Inlet protection required

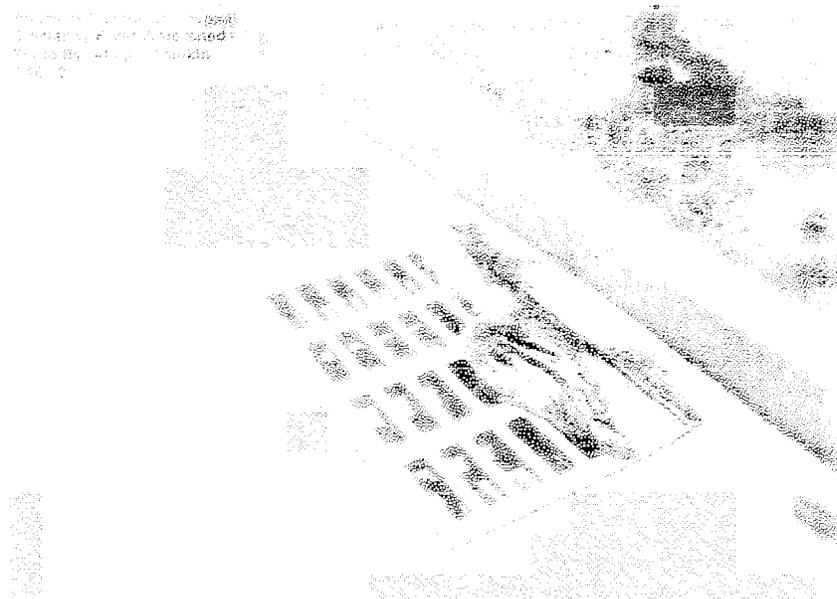


Figure 4 Must be properly maintained
City of Chicago, Department of Public Works
Chicago, Illinois

Figure 4 Must be properly maintained




Figure 5 Silt fence requires maintenance



Figure 6 Silt fence must be extended



Figure 7 Straw wattle must be properly reinstalled



Figure 8 Barren Areas
